

Active Projects 9/11/2024

Grant / Project Name	Grantor	Treatment Funds Awarded*	Activities/ Treatments to date	Remaining Treatment Funds*	Status	Exp Date
Hog & Sheep Fire Forest Restoration - CCI #619	CALFIRE	\$4,999,855.30	Biomass site prep, herbicide purchase/ application, tree planting for first two rounds of funding. Project is 75% completed.	\$1,100,000	Final operations commenced on WMB. Expect to be complete by 11/15/2024	3/31/2025
Shingletown WUI Fuels Treatments - CCI #110	CALFIRE	\$8,978,870.00	Biomass utilization 80% complete, equipment purchase 100% complete, community Treatments 50% complete, mastication treatments 95% complete, emergent brush treatments 40% complete, Community Treatments 70% complete	\$986,000	Biomass utilization ongoing. Community biomass treatments ongoing. Mastication Complete. Emergent brush treatments ongoing. Community hand thinning / defensible space ongoing. Landowner signups for community treatments ongoing, community chipping program ongoing. On Schedule to complete 12/2024	3/31/2025
Dyer Mountain WUI Fuels Treatment - CCI #0102	CALFIRE	\$5,727,260.00	Community treatments 100% complete. Emergent brush treatments 100% complete. Biomass utilization treatments 75% complete. Additional mastication acres added, 110% complete.	\$700,000	Mastication Complete. Emergent Brush ongoing. Biomass commenced Early July and ongoing on SPI and PG&E. On Schedule to complete 10/2024	3/31/2025
Whitmore Forest and Watershed Restoration - CCI #611	CALFIRE	\$4,999,989.12	Mastication 100% complete. Biomass treatments 80% complete. Emergent Brush treatments 90% complete.	\$466,000	Biomass chipping ongoing. Final emergent brush ongoing through Summer 2024. On Schedule to complete 12/2024	3/31/2025
Clear Creek & Hog Flat Fuel Treatment-Direct #112	CALFIRE	\$199,998.30	Mastication 100% complete. Hand treatments 60% complete	\$52,670	Amendment filed to add final hand crew work to agreement in area of Hamilton Branch.	3/31/2025
Eastside Communities SPA #018 / Lone Spring SNC #1275	SNC/ USFS	\$1,050,000.00	Draft EA complete. All resource specialist contracts awarded,	\$500,000	Arc surveys and wildlife surveys ongoing. Awaiting PNF to advance EA. Will seek implementation funding once signed. Will put out fall 2024 RFP for more surveys for 2025.	3/31/2031


* Does not include proprietary cost match information

Project	Grantor	Treatment Funds Awarded*	Activities/ Treatments to date	Remaining Treatment Funds*	Status	Exp. Date
Bootssole-SNC #1305	SNC	\$3,671,725.00	SPA #1 and #2 executed with PNF Beckwourth District, Timber Marking/cruising, Layout 100% complete, Mastication 100% completed, hand thinning treatments 100% completed, Biomass 100% completed.	\$300,000	Additional hand thinning acres was added to exhaust all remaining funds. Treatments will be completed 10/2024.	1/1/2025
Diamond Mountain - SNC #1065	SNC	\$882,087.00	Mastication/ pruning 100% complete. Aspen exclusion treatments 100% complete. Pile burning 90% complete. Impacted by sheep fire.	\$90,000	Prescribed burning planned for fall 2024. Contract awarded. On schedule for 12/2024 completion.	1/1/2026
Honey Lake Valley RCD/LFSC - SPA	NA	NA	MOU - SPA between organizations to assist HLVRCDC with biomass utilization, site prep, and tree planting. Biomass utilization complete on several landowners. Tree planting complete on several landowners.	NA	Biomass utilization complete. Planting complete for 2024. Herbicide planned for 2024. Reforestation planned for 2025. Additional funds remain and were added to treat more acres. Currently assessing.	NA
California Fire Safe Council County Coordinator	CFSC	\$94,827.80	2024 program ongoing.	\$55,000	2024 program active. General Meetings, CWPP, Firewise support, 6th grade education program, public outreach and community support. Collaborative group meetings and development ongoing.	12/31/2024
USFS Cradle Valley / Bootssole Dixie Fire Salvage	USFS	2,600,000	Spa complete. Layout complete.	1,700,000	Biomass Chipping to resume once contractor assembles crew. Planning for site prep. RFP planned for late September 2024 for additional salvage/ dead tree removal. Working on a 3rd SPA. Goal is to operate through fall and winter with May 2025 completion.	8/31/2026
Lassen County-Wide Defensible Space Program	CFSC	50,000	Contract awarded for implementation. Deliverables 100% complete.	66,972	Awaiting CFSC to deposit project funds. Amendment needed to add more funds to implementation. On schedule to complete 10/2024.	12/31/2024

* Does not include proprietary cost match information


Project	Grantor	Treatment Funds Awarded*	Activities/ Treatments to date	Remaining Treatment Funds*	Status	Exp. Date
Lassen County Wide Assessment	SNC	\$275,242.00	Agreement executed 7/2024.	\$275,242	RFP for assessment late summer/ fall 2024. Project	10/31/2027
South Lassen Wildfire Recovery Project	CALFIRE	\$6,469,424.33	None	\$6,469,424.33	Awaiting final agreement from calfire	3/15/2030
North Susanville WUI Fuels Treatments	CALFIRE	\$2,999,924.32	None	\$2,999,924	Awaiting final agreement from calfire	3/15/2030
LFSC LNF Dixie Fire Hazard Tree Project	CALFIRE	2,999,987.85	9/11/2024	2,999,987.85	Awaiting final agreement from calfire	3/15/2030

* Does not include proprietary cost match information

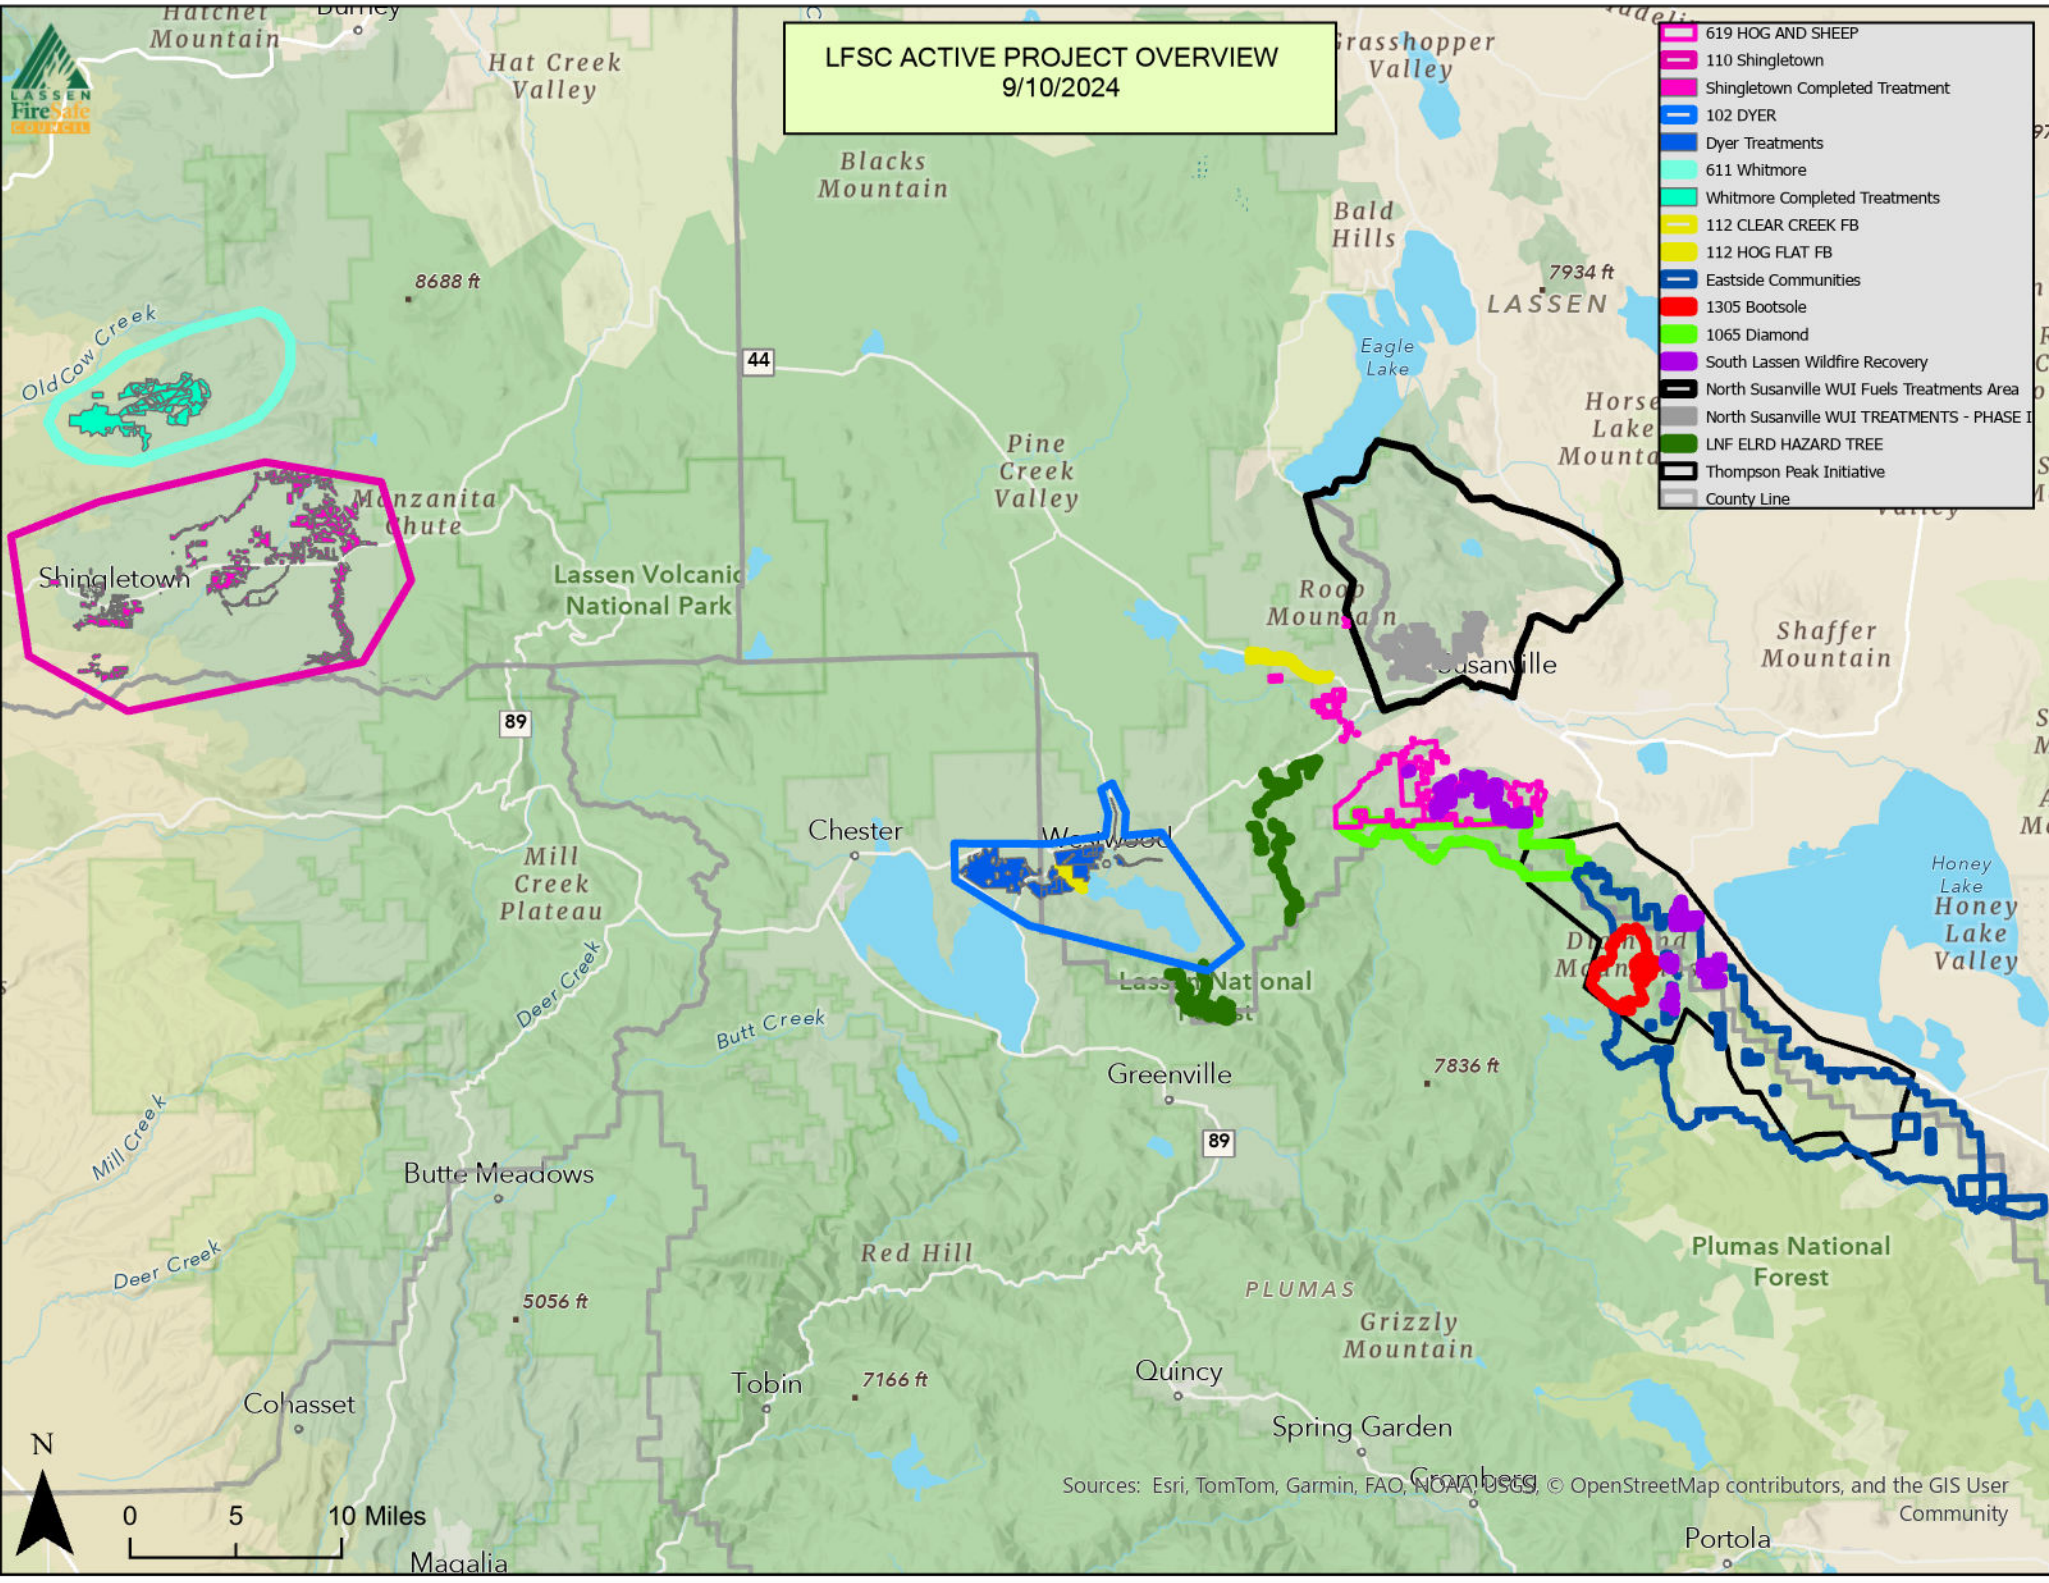

LFSC ACTIVE PROJECT OVERVIEW
9/10/2024

- ▬ 619 HOG AND SHEEP
- ▬ 110 Shingletown
- ▬ Shingletown Completed Treatment
- ▬ 102 DYER
- ▬ Dyer Treatments
- ▬ 611 Whitmore
- ▬ Whitmore Completed Treatments
- ▬ 112 CLEAR CREEK FB
- ▬ 112 HOG FLAT FB
- ▬ Eastside Communities
- ▬ 1305 Bootssole
- ▬ 1065 Diamond
- ▬ South Lassen Wildfire Recovery
- ▭ North Susanville WUI Fuels Treatments Area
- ▭ North Susanville WUI TREATMENTS - PHASE I
- ▬ LNF ELRD HAZARD TREE
- ▭ Thompson Peak Initiative
- ▭ County Line



Sources: Esri, TomTom, Garmin, FAO, NOAA, USGS © OpenStreetMap contributors, and the GIS User Community
